Divine Foods – November Roadmap and Payments


Nov 4, 2026 · @Flores Hans Harold Lee

Your new online store will be built and ready to go live by Mon 30 Nov 2026, paid in four equal payments of 25%.

This follows on from our response of 27 October. We build the store system and its connections to your existing tools first, because that takes the longest, then finish the website your customers see. Everything starts with a short handover meeting with your IT team, so we have access to what we need from day one.

9. Project roadmap (November 2026)

The store system is built first, over the first two working weeks, and the storefront is finished on top of it. The whole store is ready to go live on Mon 30 Nov.

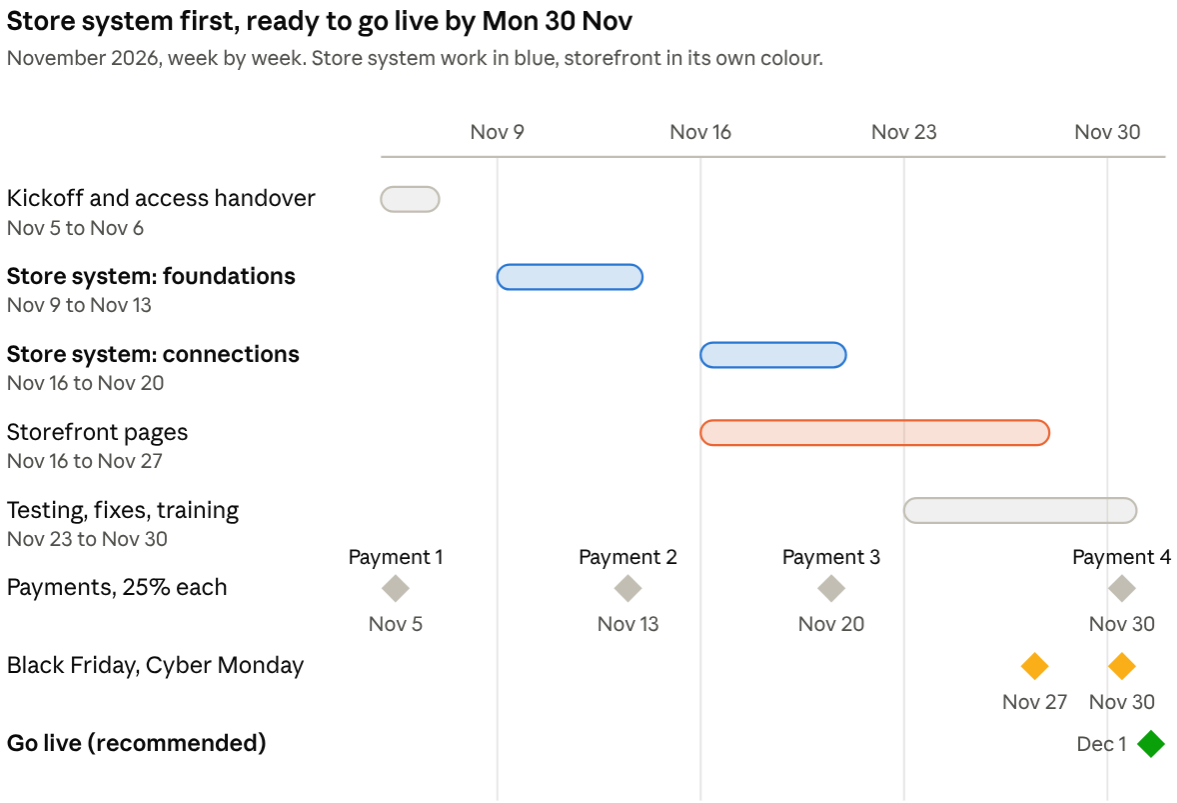

November roadmap · store system first, then storefront

1. **Thu 5 – Fri 6 Nov: Kickoff and access.** Kickoff meeting with your IT team on Thu 5 Nov. We collect the accounts, keys and system details in section 11, and set up staging and live hosting in your accounts.

2. **Mon 9 – Fri 13 Nov: Store system foundations.** Products, stock and both price lists coming in from ERPNext. Retail and café pricing. Stripe test payments. Freight quotes from your endpoint. Content editor set up. Ends with milestone 1 (payment 2).
3. **Mon 16 – Fri 20 Nov: Store system connections.** Orders sent to ERPNext, with automatic retries. Order emails through Listmonk. Enquiry forms and ERPNext leads. Uptime Kuma heartbeats. Order book, hero products, customer sign-in and the AI assistant's limits. Storefront pages start on staging once the foundations are in. Ends with milestone 2 (payment 3).
4. **Mon 23 – Fri 27 Nov: Storefront finished.** Every page connected to the store system, plus checkout, analytics, redirects and legal pages. Your team tests on staging from Mon 23 Nov.
5. **Sat 28 – Mon 30 Nov: Fixes, training and handover.** Final fixes, the recorded training session and handover notes. Ready to go live on Mon 30 Nov (payment 4), with the switch-over recommended for Tue 1 Dec.

10. Payments and what you receive

The project is paid in four payments of 25%. Each one is tied to something you can see and test, not to a date alone.

Payment	Due	Tied to	What you receive
1 – 25%	On signing (target Thu 5 Nov)	Project start	Kickoff meeting with your IT team; the access checklist (section 11); this roadmap confirmed; staging and live environments set up in your accounts by Wed 11 Nov
2 – 25%	Fri 13 Nov	Store system foundations working on staging	Products, stock and both price lists coming in from ERPNext; retail and café prices showing correctly; Stripe test payments; freight quotes from your endpoint; admin dashboard and content editor logins; a short demo recording

Payment	Due	Tied to	What you receive
3 – 25%	Fri 20 Nov	Store system complete on staging	Orders sent to ERPNext with delivery dates and addresses; order emails through Listmonk; enquiry forms to the right inbox plus ERPNext leads; Uptime Kuma heartbeats; order book; hero products; customer sign-in; the AI assistant's content and limits; first storefront pages on staging; demo recording
4 – 25%	Mon 30 Nov	Whole store ready to go live	Finished storefront on staging, tested end to end; checkout, sign-in and AI chat working; Google Analytics tracking; approved list of 301 redirects; legal pages ready for your wording; recorded training session; handover notes; all code in your GitHub. IP transfers to Divine Foods on this payment

Invoices are issued on each milestone with 7-day payment terms, and show GST where it applies.

Signing off a milestone

- We send a staging link, a short demo recording and a checklist of what to test.
- You have 2 business days to approve it or tell us about any problems in writing.
- Only serious problems (something broken or wrong for customers) hold up sign-off. Small fixes are listed and done in the following week.
- If we hear nothing within 2 business days, the milestone counts as approved.

If something we need arrives late

The dates assume we receive the items in section 11 on time. If access or information arrives late, the dates after it move by the same number of days. We'll always tell you straight away if something is holding us up.

Going live

Payment 4 is due when the store is ready to go live, not on the day you choose to switch over. Black Friday is Fri 27 Nov and Cyber Monday is Mon 30 Nov. We recommend keeping your current site running through both, and switching to the new store on Tue 1 Dec. That puts your whole Christmas period inside the free first month of support.

11. What we need from your IT team

We need the first group of items by Fri 6 Nov, because the store system work starts on Mon 9 Nov and depends on them. We'll go through this list together at the kickoff meeting on Thu 5 Nov.

How to share passwords and keys safely

- Please set up a shared folder in your password manager (for example 1Password or Bitwarden) and share it with our named team members. Everything below goes there.
- Please never send passwords or keys by email, chat or text message.
- Live payment keys are entered by you directly into your hosting accounts, so we never need to see them.
- Each account stays in Divine Foods' name, with the lowest level of access that lets us do the work. You can remove us at any time.

Accounts and access

System	What you set up	What you share with us	By
Password manager	A shared folder for this project	Invite for our team	Thu 5 Nov
ERPNext	A separate user just for the website, with access only to products, prices, stock, customers, sales orders and leads. A test copy of ERPNext if you have one	Web address, the user's key and secret, ERPNext version	Fri 6 Nov
Freight quote endpoint	A login just for the website, and a test mode if available	Web address, login details, example requests and replies	Fri 6 Nov
Listmonk	A website user that can only send emails, read templates and add newsletter sign-ups	Web address, user name and key, Listmonk version	Fri 6 Nov

System	What you set up	What you share with us	By
GitHub	An organisation owned by Divine Foods (at least two owners from your team)	Invite us as collaborators on the store repositories	Fri 6 Nov
Railway (store hosting)	A Pro workspace with separate staging and live projects	Invite us as "Member" (you keep billing and admin)	Fri 6 Nov
Stripe	Your Stripe account, activated with business and bank details	Invite us as "Developer" (or "Sandbox" during the build); test keys only	Fri 6 Nov
Uptime Kuma	Monitors for the website and each background job	One heartbeat link per monitor, and who gets alerts	Wed 11 Nov
Vercel (website hosting)	A Pro team	Invite us as "Developer"	Wed 11 Nov
Domain and DNS	No change yet	A contact who can add records, and your current DNS settings	Wed 11 Nov
Google Analytics	Your GA4 property (and Tag Manager or ad accounts if you use them)	Editor access	Wed 11 Nov
Sentry (error tracking)	An organisation in your name	Invite us as a member	Wed 11 Nov
AI assistant	An account in your name with a monthly spending limit	Developer access to that workspace only	Wed 11 Nov
Google and Microsoft sign-in	A Google Cloud project and a Microsoft app registration, under a company email such as it@	Add us as developers	Wed 11 Nov
Facebook sign-in	A Meta developer app	Add us as developer; we'll submit it for Meta's approval early	Wed 11 Nov

System	What you set up	What you share with us	By
Apple sign-in	An Apple Developer account for Divine Foods. If you don't have one, please start the sign-up on Thu 5 Nov, as Apple's checks can take one to three weeks	Add us as developer once approved	Start Thu 5 Nov

Please describe your existing systems for us (by Fri 6 Nov)

A short document or spreadsheet is fine. This is what lets us connect to your tools without guessing.

- **ERPNext:** the exact names of the retail and café price lists; whether prices include GST; how item codes work and which items are sold online; where shelf life, allergens and ingredients are stored; which warehouse sets online stock; how approved café customers are marked; which fields a sales order needs, including delivery dates and how card payments are recorded; and any automations that run when an order or customer is created.
- **Listmonk:** the version you run; the newsletter list or lists and opt-in setting; the email templates to use for order confirmation, shipping, password reset and enquiries; and the sender address for each.
- **Freight endpoint:** what it expects and returns (postcode, carton or pallet sizes and weights, service, price, delivery estimate); error messages; how long a quote stays valid; and your BigPost limit.
- **Email inboxes:** confirm that cafes@, sales@ and info@ are set up.
- **Current website:** admin access or a list of current page addresses (for the redirects), and any tracking codes in use.
- **Decisions:** whether subscriptions are in scope, where chat notifications should go, and who will approve the legal page wording.
- **Contacts:** a main IT contact for each system, and when changes are not allowed (for example, during month-end).

12. If anything slips

November is a tight window, so we've agreed in advance which items can move into early December without holding up your launch. Anything on this list would be finished inside the free first month of support, at no extra cost.

- **Best-seller heroes:** heroes are hand-picked at launch anyway (section C1). The automatic switch to sales data only starts once there's enough sales history.

- **Apple, Facebook and Shop sign-in:** these need approval from Apple, Meta or Shopify, which we don't control. If approval isn't through by Wed 25 Nov, we launch with email, Google and Microsoft sign-in and switch the others on as soon as they're approved.
- **Subscriptions:** if you confirm they're in scope, and the details aren't settled by Fri 13 Nov, we'd launch one-off orders first and add recurring orders in early December.
- **AI chat assistant:** if it needs more testing, the store launches with the enquiry form and the assistant follows shortly after.

Nothing on this list affects taking orders, payments, pricing, freight, emails or the sync to ERPNext. Those are all ready for launch.

Appendix: setting names for your IT team

These are the settings we'll create in your hosting accounts. Most are generated inside the hosting tools; the ones marked "from you" come from your existing systems. Staging and live each get their own values.

Where	Setting	Comes from
Railway (store system)	`DATABASE_URL`, `REDIS_URL`	Created in Railway
Railway	`JWT_SECRET`, `COOKIE_SECRET`	Generated in Railway, different per environment
Railway	`STORE_CORS`, `ADMIN_CORS`, `AUTH_CORS`, `MEDUSA_BACKEND_URL`	Your website and admin addresses
Railway	`MEDUSA_WORKER_MODE`, `DISABLE_MEDUSA_ADMIN`	Set by us (separate server and background worker)
Railway	`STRIPE_API_KEY`, `STRIPE_WEBHOOK_SECRET`	From you: test keys now, live keys entered by you at launch
Railway	ERPNext address, API key and secret	From you
Railway	Listmonk address, API user and token, template IDs	From you
Railway	Freight endpoint address and login	From you
Railway	Uptime Kuma heartbeat links (one per job)	From you
Railway	Google, Microsoft, Apple and Facebook sign-in IDs and secrets	From you (each app in Divine Foods' name)

Where	Setting	Comes from
Vercel (website)	`NEXT_PUBLIC_MEDUSA_BACKEND_URL`, `NEXT_PUBLIC_MEDUSA_PUBLISHABLE_KEY`	Set by us
Vercel	`NEXT_PUBLIC_STRIPE_KEY`	Stripe publishable key (test now, live at launch)
Vercel	`PAYLOAD_SECRET`, content editor database and file storage key	Generated in Vercel
Vercel	`ANTHROPIC_API_KEY`	From your AI assistant account, one key per environment
Vercel	Google Analytics measurement ID	From you
Both	`SENTRY_DSN`, `SENTRY_AUTH_TOKEN`, `SENTRY_ORG`, `SENTRY_PROJECT`	From your Sentry organisation

A few names may differ slightly depending on the final versions of each tool. We'll confirm the full list at kickoff.
